

PROJECT UPDATE

Mandan, North Dakota

for the weeks of
8.26 & 9.02
2019

General Overview:

Mariner Construction is repaving several blocks within the Southside neighborhood! This project will be on-going through this fall with final completion expected in June of 2020. Generally, the order of construction will be as follows:

1. Removals, 2. Pipe installation, 3. Concrete work, 4. Aggregate base, 5. Asphalt paving, 6. Restoration/Seeding, 7. Chip sealing (2020). On the north side of the neighborhood, the contractor is working to finish up the stabilized base and concrete repairs, and will soon be paving north of 3rd Street. On the south side of the neighborhood, the pipe installation crew is starting the installation of the new storm sewer pipe.

What To Expect?


- The contractor will place no-parking signs several days in advance, where the crews will be working.
- Expect dust, noise and minor inconveniences normally associated with construction.
- Working hours will likely be approximately 7 a.m. – 7 p.m., 5 days per week.
- If you have sprinklers that have been damaged, please notify the on-site engineer.
- Traffic control barricades will be placed to protect both travelers and workers.
- Isolated street closures will be temporary, but may last a few days.
- Roadways will re-opened with a temporary gravel surface until they are paved. Drive slowly as there are areas of uneven pavement.
- The contractor will be spreading water on temporary gravel streets to keep dust down.
- Freshly poured concrete cannot be driven on, so barricades will remain up until it has achieved the proper strength for traffic.

The Next Two Weeks:

- Similar to the last few weeks, there are two crews working on underground piping, two crews working on concrete patches, and one crew working on street replacement.
- The contractor will be re-grading several streets and stabilizing the soils with cement treatment to get them ready for asphalt paving.
- In certain locations, City boulevards will be getting re-graded to match new pedestrian ramps.

Detour Planned:

In a few weeks, a detour will be needed to finish up some storm sewer inlets within 3rd St and 7th Ave, and 3rd St and 6th Ave. More information to come as the detour time approaches.

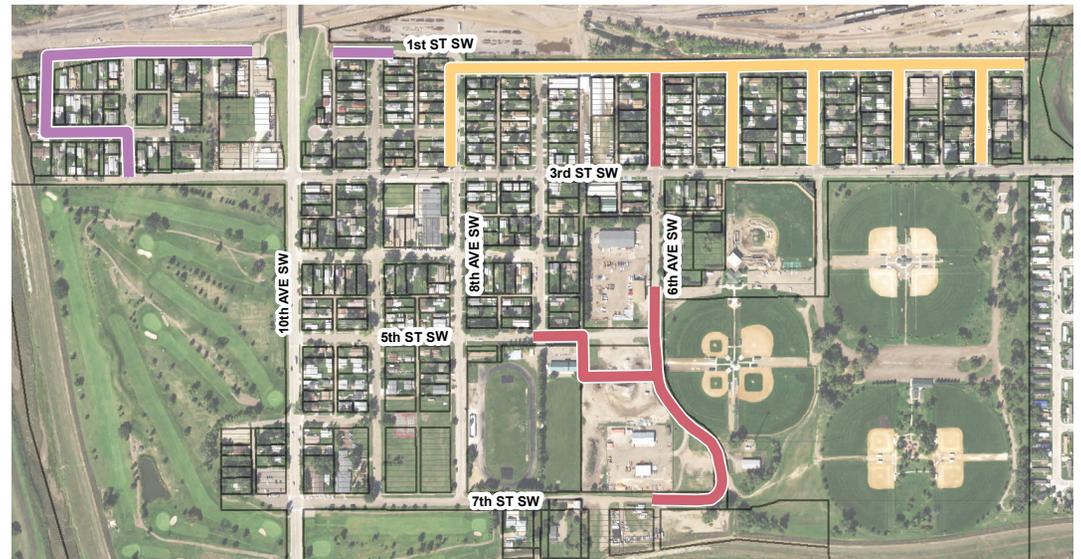

Project CONTACTS

The City of Mandan has contracted with Moore Engineering for the construction engineering of the improvements. Michael Gorder will be the on-site engineer throughout the construction and can be reached at 651-328-3354 to discuss concerns. A weekly construction meeting, open to the public, will be held on Tuesday mornings from 11:00 a.m. – 11:30 a.m. in the conference room of the Public Works Shop at 411 6th Ave SW.

Watch the website for updated construction map every 2 weeks. Thank you in advance for your patience through the construction process!

